Project:	Stanstead Radial Gate Replacement	**Prepared By:**	DAP
Code:	BAU.5430		

Commencing:	05/08/24
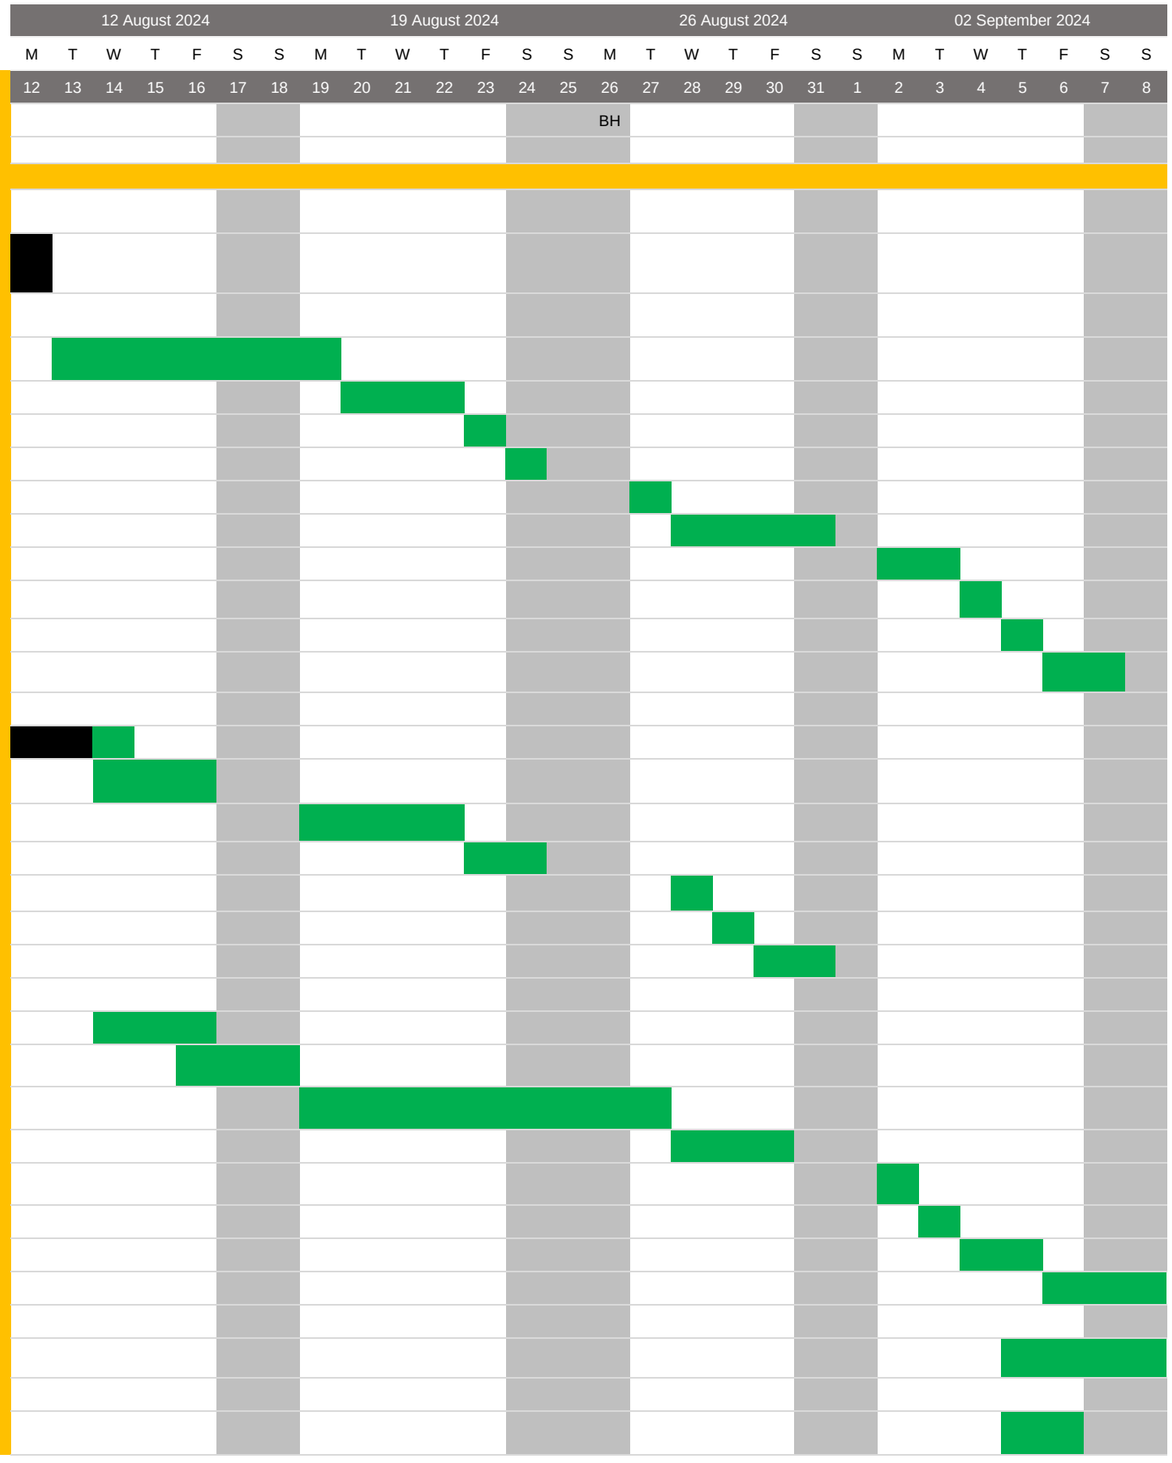
Task	Responsible team	Planned Start	Planned End	As-built Start	As-built End
Site Operations					
Down Stream central wall					
Remove shutter Saturday weekend working only. Excavator on the bridge for short periods to move components from the sluice to the yard for cleaning and dismantling.	BAM	10/08/24	12/08/24	10/08/24	12/08/24
Down Stream East wall					
Install formwork panels taken from compound to work area. Only Saturday working at the weekend	BAM	13/08/24	19/08/24	13/08/24	
Prep for concrete pour (temp works) Lift 1	BAM	20/08/24	22/08/24		
Concrete pour Lift 1 Concrete wagon sitting on the road for 25 mins *3 trips. Cars will be able to pass.	BAM	23/08/24	23/08/24		
Strike shutter Lift 1	BAM	24/08/24	24/08/24		
Remove shutter Lift 1 Excavator movements to the yard	BAM	27/08/24	27/08/24		
Install formwork Lift 2 Excavator movements from the yard	BAM	28/08/24	31/08/24		
Prep for concrete pour Lift 2	BAM	02/09/24	03/09/24		
Concrete pour Lift 2 Concrete wagon sitting on the road for 25 mins *3 trips. Cars will be able to pass.	BAM	04/09/24	04/09/24		
Strike shutter Lift 2	BAM	05/09/24	05/09/24		
Remove and clean shutters Lift 2 Excavator movements to the yard.	BAM	06/09/24	07/09/24		
Up Stream central wall					
Install temporary works for US central wall	BAM	13/08/24	14/08/24	12/08/24	13/08/24
Install rebar Weekend works (Saturday and Sunday) Excavator and transit vehicle taking rebar from the yard to the site	BAM	14/08/24	16/08/24	14/08/24	
Install formwork Excavator movements from the yard.	BAM	19/08/24	22/08/24		
Prep for concrete pour (temp works) Saturday weekend working only.	BAM	23/08/24	24/08/24		
Concrete pour Concrete wagon sitting on the road for 25 mins *3 trips. Cars will be able to pass.	BAM	28/08/24	28/08/24		
Strike shutter	BAM	29/08/24	29/08/24		
Remove and clean shutter Excavator movements to the yard	BAM	30/08/24	31/08/24		
Up Stream East wall					
Install temporary works for US East wall	BAM	14/08/24	16/08/24	14/08/24	
Install rebar Reinforcement installed over the weekend, Saturday & Sunday. Excavator and transit taking rebar from the yard to the site	BAM	16/08/24	18/08/24		
Install formwork Lift 1 Excavator to move components from the yard to the sluice. Only potential Saturday work during the Bankholiday weekend	BAM	19/08/24	27/08/24		
Prep for concrete pour (temp works) Lift 1	BAM	28/08/24	30/08/24		
Concrete pour Lift 1 Concrete wagon sitting on the road for 25 mins *3 trips. Cars will be able to pass.	BAM	02/09/24	02/09/24		
Strike shutter Lift 1	BAM	03/09/24	03/09/24		
Remove shutter Lift 1 Shutter stays in the sluice. Minimal interface	BAM	04/09/24	05/09/24		
Install formwork Lift 2 Some additional shutters moved from the compound	BAM	06/09/24	10/09/24		
Ground Strengthening					
Setup geobear DS They operate from a transit van planned to be parked within the site. Drilling activities will be noisy	BAM	05/09/24	08/09/24		
Weep holes					
Repair existing weep holes and install new one. All within the sluice. Kilnbridge operate from Transit vbans. Drilling activities will be noisy	Kilbridge / BAM	05/09/24	06/09/24
