| | | | |
|---|---|---|---|
| **Project:** | Stanstead Radial Gate Replacement | **Prepared By:** | DAP |
| **Code:** | BAU.5430 | | |

| Commencing: | 26/08/24 |
|---|---|
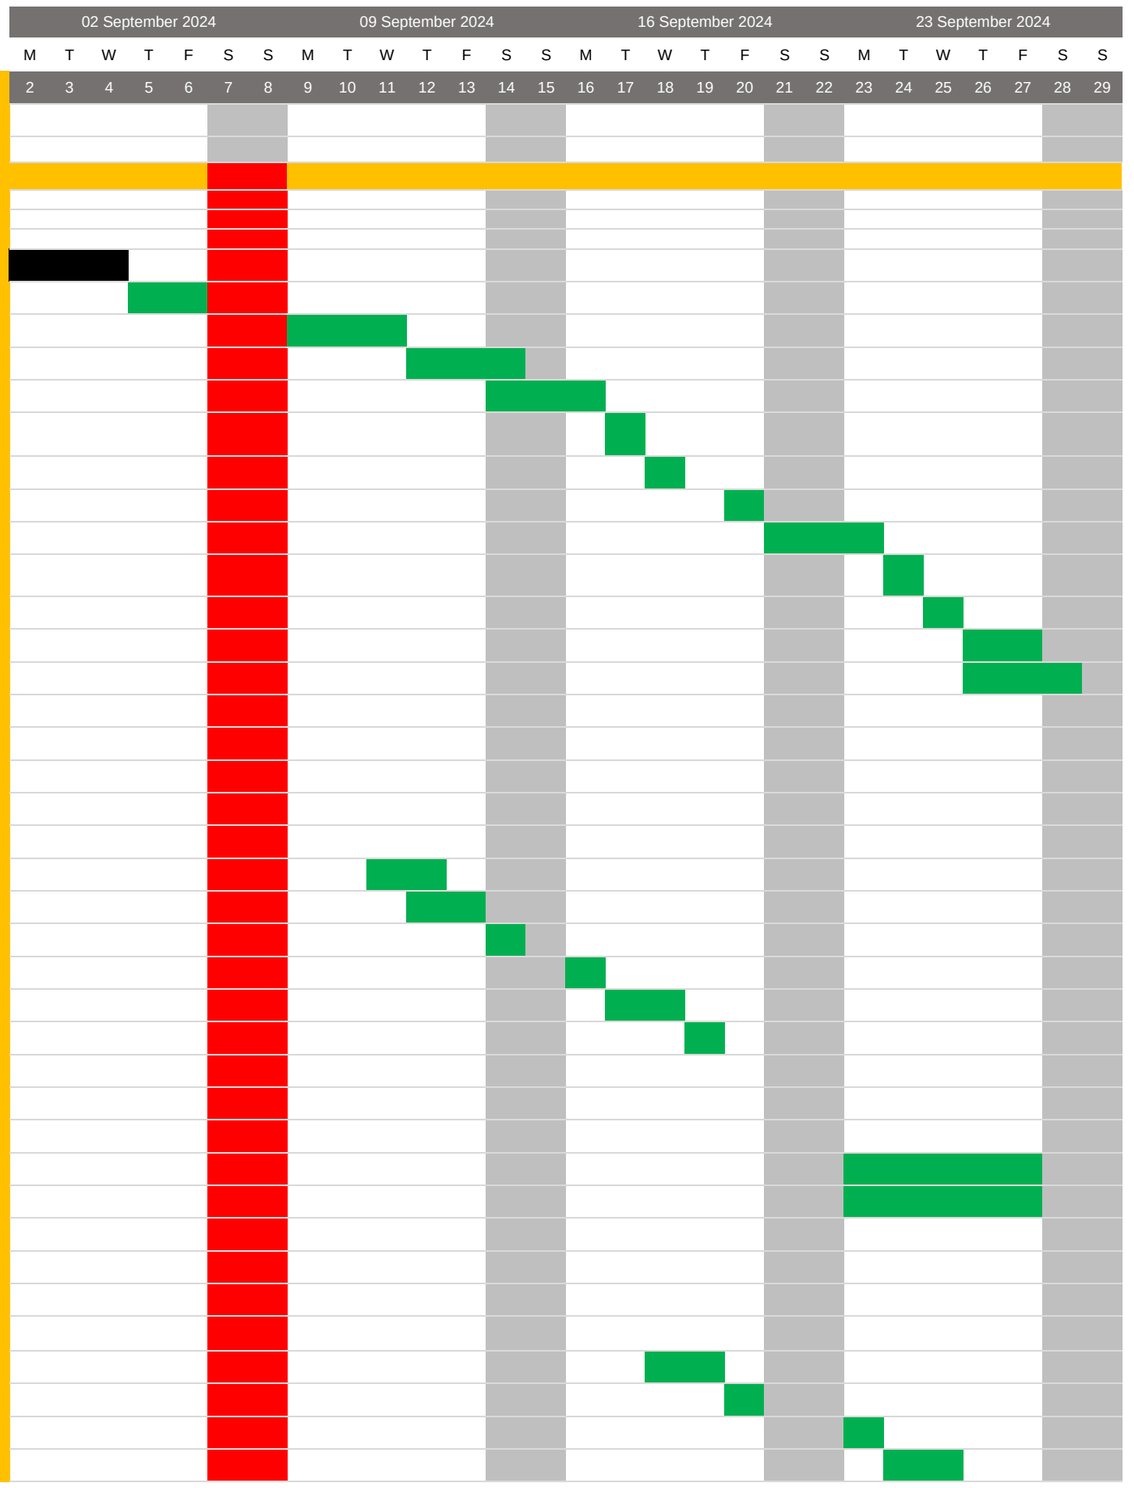
| Task | Responsible team | Planned Start | Planned End | As-built Start | As-built End |
|---|---|---|---|---|---|
| **Site Operations** | | | | | |
| **US East wall** | | | | | |
| Repairs to stop log cill | BAM | 30/08/24 | 04/09/24 | 30/08/24 | 04/09/24 |
| Reinstall stop logs Excavator movements to the yard | BAM | 05/09/24 | 06/09/24 | | |
| Dewater and Clean out sluice Excavator movements to the yard | BAM | 09/09/24 | 11/09/24 | | |
| Strip and clean US formwork | BAM | 12/09/24 | 14/09/24 | | |
| Re-Install formwork and prep for pour | BAM | 14/09/24 | 16/09/24 | | |
| Concrete pour Lift 1 Concrete wagon sitting on the road for 25 mins *3 trips. Cars will be able to pass. | BAM | 17/09/24 | 17/09/24 | | |
| Strike shutter Lift 1 | BAM | 18/09/24 | 18/09/24 | | |
| Remove shutter Lift 1 Shutter stays in the sluice. Minimal interface | BAM | 20/09/24 | 20/09/24 | | |
| Install formwork Lift 2 Excavator movements to the yard | BAM | 21/09/24 | 23/09/24 | | |
| Concrete pour Lift 2 Concrete wagon sitting on the road for 25 mins *3 trips. Cars will be able to pass. | BAM | 24/09/24 | 24/09/24 | | |
| Strike shutter Lift 2 | BAM | 25/09/24 | 25/09/24 | | |
| Remove shutter Lift 2 Excavator movements to the yard | BAM | 26/09/24 | 27/09/24 | | |
| Install formwork Lift 3 Excavator movements to the yard | BAM | 26/09/24 | 28/09/24 | | |
| Concrete pour Lift 3 Concrete wagon sitting on the road for 25 mins *3 trips. Cars will be able to pass. | BAM | 30/09/24 | 30/09/24 | | |
| Strike shutter Lift 3 | BAM | 01/10/24 | 01/10/24 | | |
| Remove shutter Lift 3 Excavator movements to the yard | BAM | 02/10/24 | 03/10/24 | | |
| | | | | | |
| **Ground Strengthening** | | | | | |
| Setup geobear | BAM | 11/09/24 | 12/09/24 | | |
| Undertake DS works Drillnig and pumping works may be relatively noisy | BAM | 12/09/24 | 13/09/24 | | |
| Demobilise DS Excavator movements to the yard | BAM | 14/09/24 | 14/09/24 | | |
| Setup geobear US | BAM | 16/09/24 | 16/09/24 | | |
| Undertake US works Drillnig and pumping works may be relatively noisy | BAM | 17/09/24 | 18/09/24 | | |
| Demobilise US Excavator movements to the yard | BAM | 19/09/24 | 19/09/24 | | |
| | | | | | |
| Site review of work scope | Paktronic | 20/06/24 | 04/07/24 | 20/06/24 | 27/06/24 |
| **8. & 9. Control Building Electrical strip out** | | | | | |
| Electrical Strip Out A couple on vans parking near the work area. | Hunton | 23/09/24 | 27/09/24 | | |
| Rearrangement existing equipment for MCC extension | Paktronic | 23/09/24 | 27/09/24 | | |
| Repair the sluice gate control panel | Client | 29/08/24 | 30/08/24 | | |
| | | | | | |
| **Removal of sluice work equipment** | | | | | |
| Install new stop logs DS (test) Lorry to bring stop logs from compound to work area. | BAM | 16/09/24 | 17/09/24 | | |
| Remove access and equipment from DS sluice Excavator movements to the yard | BAM | 18/09/24 | 19/09/24 | | |
| Remove existing stop logs DS flood work area Lorry to bring stop logs from compound to work area. | BAM | 20/09/24 | 20/09/24 | | |
| Install insert into US Right bank Stop log | Hunton | 23/09/24 | 23/09/24 | | |
| Install side rails for gantry crane to accomondate new stop logs DS. Lorry to bring materials from compound to work area. | BAM | 24/09/24 | 25/09/24 | | |
