Project:	Stanstead Radial Gate Replacement	Prepared By:	DAP
Code:	BAU.5430		

Commencing:	30/09/24
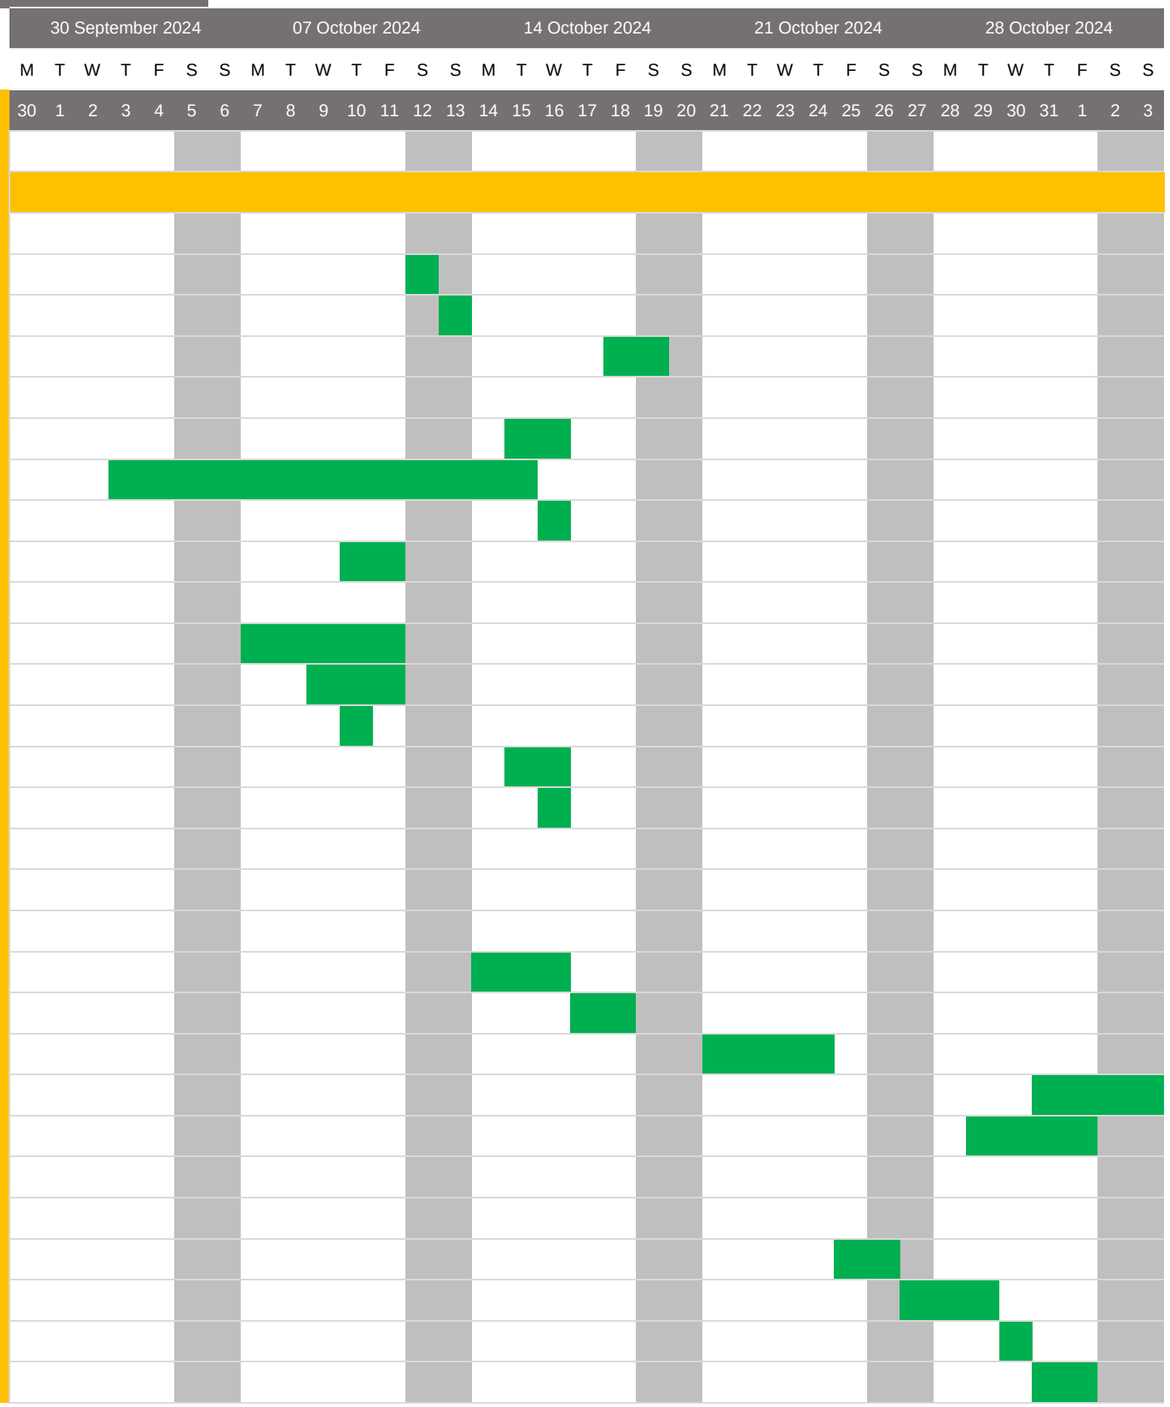
Task	Responsible team	Planned Start	Planned End	As-built Start	As-built End
Site Operations					
Cruising club Dates					
Last Cruise	BAM	12/10/24	12/10/24		
Timbers out ready for Cranage of boats	BAM	13/10/24	13/10/24		
Remove boats from the river	BAM	18/10/24	19/10/24		
Removal of sluice work equipment					
Install cross bracing DS Excavator working on the bridge for short periods	BAM	15/10/24	16/10/24		
Install cross bracing US Excavator bringing props to site from compound	BAM	03/10/24	15/10/24	05/10/24	
Install new stop logs US (test)	BAM	16/10/24	16/10/24		
Fix side rails for gantry crane new stop logs US part 2	BAM	10/10/24	11/10/24		
Place stop logs for winter operations US Excavator movement from compound	BAM	11/10/24	09/10/24		
Remove 450mm inline pump Large lorries with Hiab or BAM excavator	BAM	07/10/24	11/10/24		
remove 12" over pumping system Large lorries with Hiab or BAM excavator	BAM	09/10/24	11/10/24		
Make good roadway to CC gate	BAM	10/10/24	10/10/24		
Clean and clear site Divers using compressor. Crane on site	BAM	15/10/24	16/10/24		
Training for EA filed team operatives	BAM / EA	16/10/24	16/10/24		
WINTER 2024					
Install ducting and pits					
UKPN to A6 to bridge Materials brought over the West side embankment	BAM	14/10/24	16/10/24		
A6 to A7 to Bridge & light column Materials brought over the West side embankment	BAM	17/10/24	18/10/24		
Potential UKPN kiosk to junction pit Materials brought over the West side embankment	BAM	21/10/24	24/10/24		
Routes A10 - C2 - C1 - A2	BAM	31/10/24	07/11/24		
Run temporary cable too Control building and site compound	Hunton's	29/10/24	01/11/24		
7. Internal and external repairs to control building.					
Excavate foundations for building extension Material movement from the West side embankment	BAM	25/10/24	26/10/24		
Formwork and rebar	BAM	27/10/24	29/10/24		
Concrete Concrete lorry delivery	BAM	30/10/24	30/10/24		
Strike and remove temporary works	BAM	31/10/24	01/11/24
