Project:	Stanstead Radial Gate Replacement	Prepared By:	DAP
Code:	BAU.5430		

Commencing:	04/11/24
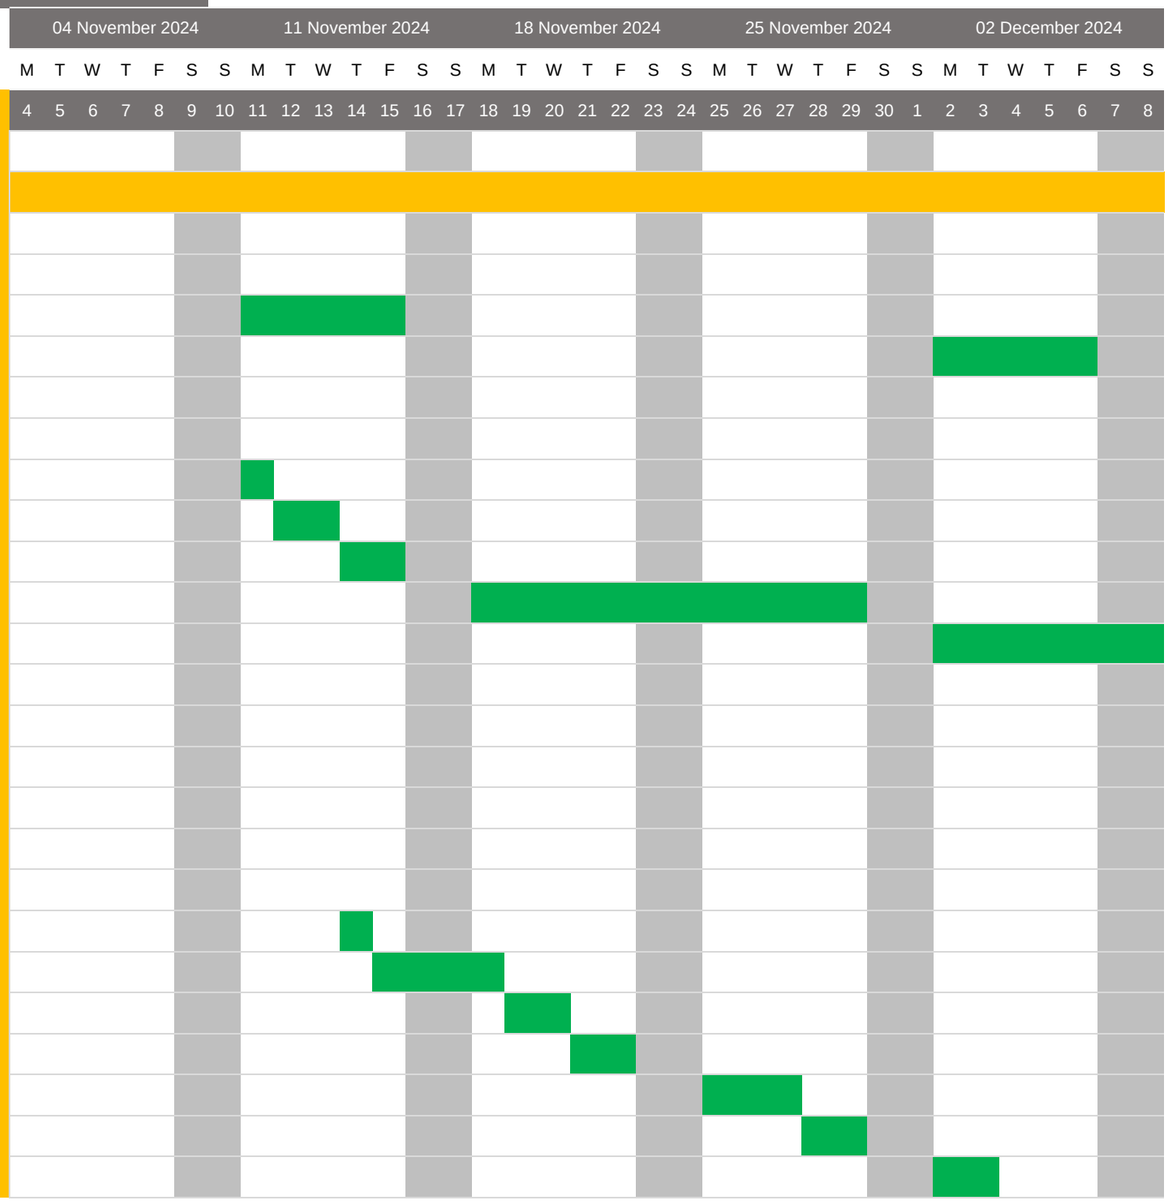
Task	Responsible team	Planned Start	Planned End	As-built Start	As-built End
Site Operations					
WINTER 2024					
Install ducting and pits					
Routes C3 - C2 - C1 - A5 including spurs	BAM	11/11/24	15/11/24	30/10/24	
Routes A5 - A8 - B3	BAM	02/12/24	06/12/24		
7. Internal and external repairs to control building.					
Strike and remove temporary works	BAM	11/11/24	11/11/24	05/11/24	
Remove brickwork West face for tie in	BAM	12/11/24	13/11/24		
Clear excess materials from existing roof structure	BAM	14/11/24	15/11/24		
Install new brickwork for building extension	BAM	18/11/24	29/11/24		
Place roof section and support beams	BAM	02/12/24	09/12/24		
Move front door into new entrance way	BAM	10/12/24	11/12/24		
Remove old internal structure	BAM	12/12/24	13/12/24		
Prepare internal structure for new equipment	BAM	16/12/24	18/12/24		
Install guttering and other external finishings	BAM	19/12/24	20/12/24		
Install upgraded bypass pipe chamber					
Close by pass pipe and bung at US inlet	BAM	14/11/24	14/11/24		
Excavate for new bypass chamber	BAM	15/11/24	18/11/24		
Install blinding	BAM	19/11/24	20/11/24		
Remove old pipework	BAM	21/11/24	22/11/24		
Install new pipework	BAM	25/11/24	27/11/24		
Install new rings including concrete surround	BAM	28/11/24	29/11/24		
Bench inside manhole, place weep hole etc	BAM	02/12/24	03/12/24
