Project:	Stanstead Radial Gate Replacement	Prepared By:	DAP
Commencing:	04/08/25		
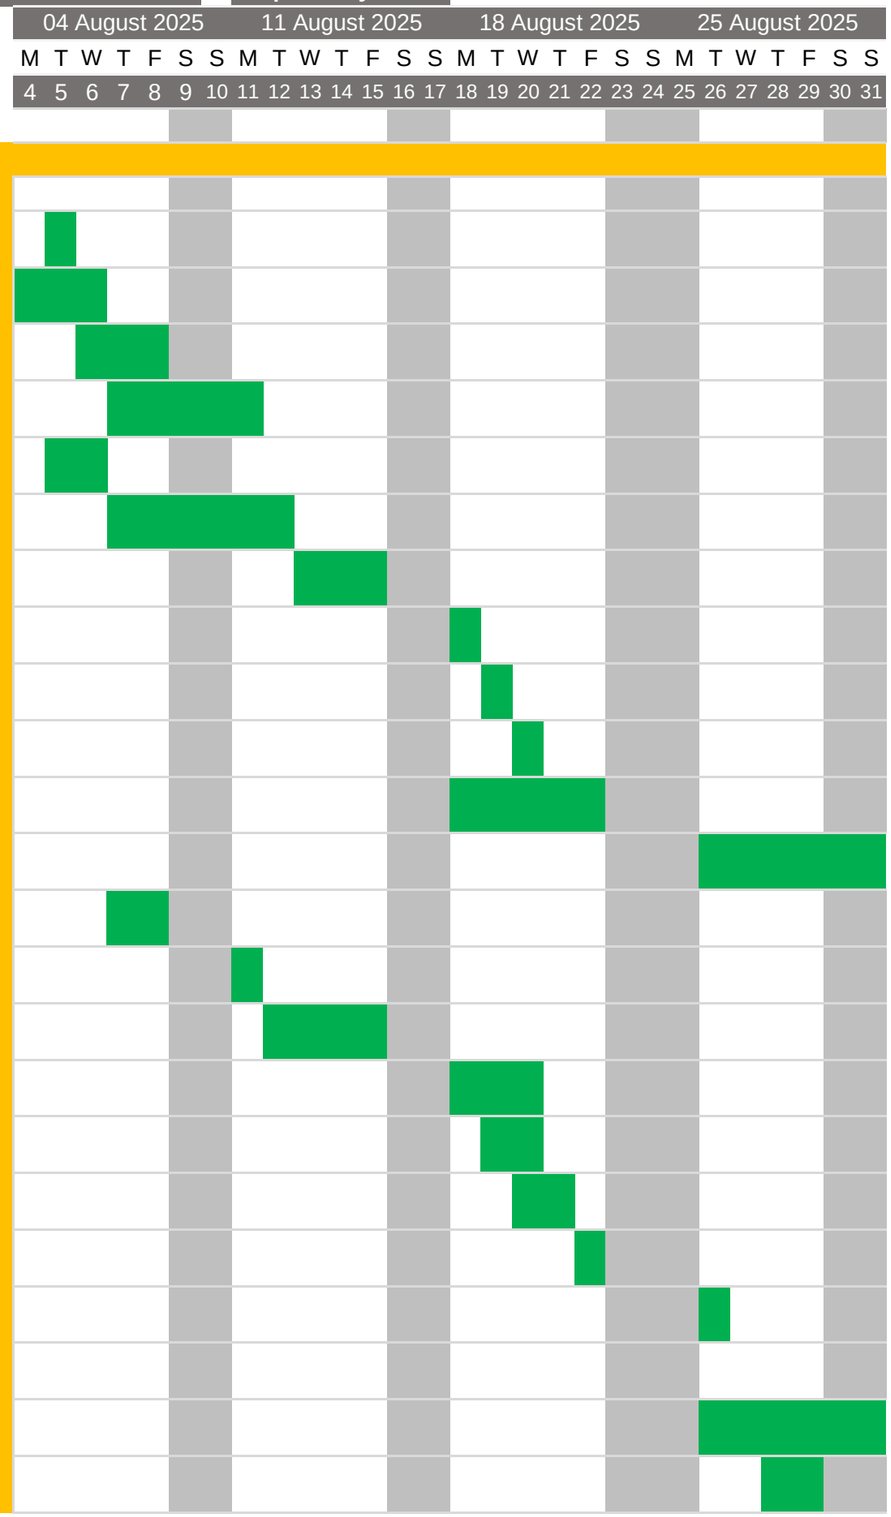
Task	Responsible team	Planned Start	Planned End	As-built Start	As-built End
Site Operations					
Summer 2025					
Concrete base slab Completed	BAM	05/08/25	05/08/25	01/08/25	01/08/25
Wall B invert starter bars	BAM	04/08/25	06/08/25	04/08/25	
Wall B wall ties Drilling and small tools	BAM	06/08/25	08/08/25	04/08/25	
Install formwork for Wall A RH channel Crane operations and transport of shutters from compound toworks area.	BAM	07/08/25	11/08/25	04/08/25	
Scabble Wall A existing end walls and base slab. VERY NOISY ACTIVITY. Tuesday 10:00 - 17:00 and most of Wednesday	BAM	05/08/25	06/08/25		
Install reinforcement	BAM	07/08/25	12/08/25		
Install formwork for Wall A LH channel Crane operations and transport to site	BAM	13/08/25	15/08/25		
Preparation for concrete pour	BAM	18/08/25	18/08/25		
Concrete Wall A Concrete lorry set up near access road. Vehicles will be able to pass. No pedestrian restrictions	BAM	19/08/25	19/08/25		
Strike formwork Wall A Crane operations and transport to compound	BAM	20/08/25	20/08/25		
Wall B steelwork	BAM	18/08/25	22/08/25		
Wall B 1st Lift Formwork Crane operations and transport to site	BAM	26/08/25	01/09/25		
RB Up & Over Install scaffold access Scaffolders lorry tem,porarily parked on E-W trackway. Willmove if Club Car arrives	BAM	07/08/25	08/08/25		
RB Up & Over Cut front face Noisy works similar to cutting operations 2 weeeks ago	Kilnbridge	11/08/25	11/08/25		
RB Up & Over Remove steps Excavator with breaker. Noisy works	BAM	12/08/25	15/08/25		
RB Up & Over Place formwork channel side Crane operations Smaill shutters required	BAM	18/08/25	20/08/25		
RB Up & Over Place steelwork	BAM	19/08/25	20/08/25		
RB Up & Over Complete formwork	BAM	20/08/25	21/08/25		
RB Up & Over Pour Concrete Concrete lorry set up near access road. Vehicles will be able to pass. No pedestrian restrictions	BAM	22/08/25	22/08/25		
RB Up & Over Strike Shutters	BAM	26/08/25	26/08/25		
Mechanical & Electrical					
Install Gate RB including cheek plate	Hunton's	26/08/25	12/09/25		
Install Secondary Bridge (temp) Crane operations and transport to site	BAM	28/08/25	29/08/25
